

# **Review of Environmental Factors**

## **Hunter-Central Coast REZ Network Infrastructure**

**Appendix K – Traffic Assessment**

**Wired for good.™**



# Traffic Impact Assessment

07-Jul-2025

Hunter-Central Coast Renewable Energy Zone Network Infrastructure Project

**Commercial-in-Confidence**

# Traffic Impact Assessment

Client: Ausgrid

ABN: 20 093 846 925

Prepared by

**AECOM Australia Pty Ltd**

Gadigal Country, Level 21, 420 George Street, Sydney NSW 2000, PO Box Q410, QVB Post Office NSW 1230, Australia

T +61 1800 868 654 [www.aecom.com](http://www.aecom.com)

ABN 20 093 846 925

07-Jul-2025

Job No.: 60751984

AECOM in Australia and New Zealand is certified to ISO9001, ISO14001 and ISO45001.

© AECOM Australia Pty Ltd (AECOM). All rights reserved.

AECOM has prepared this document for the sole use of the Client and for a specific purpose, each as expressly stated in the document. No other party should rely on this document without the prior written consent of AECOM. AECOM undertakes no duty, nor accepts any responsibility, to any third party who may rely upon or use this document. This document has been prepared based on the Client's description of its requirements and AECOM's experience, having regard to assumptions that AECOM can reasonably be expected to make in accordance with sound professional principles. AECOM may also have relied upon information provided by the Client and other third parties to prepare this document, some of which may not have been verified. Subject to the above conditions, this document may be transmitted, reproduced or disseminated only in its entirety.

## Quality Information

Document Traffic Impact Assessment  
 Ref 60751984  
 Date 07-Jul-2025  
 Originator Jordan Shiu  
 Checker/s Sara Hu  
 Verifier/s Brigitte Humphrey-Robinson

## Revision History

Rev	Revision Date	Details	Approved	
			Name/Position	Signature
A	23-Apr-2025	For review	Brigette Humphrey-Robinson Team Leader - Transport Planning & Advisory	<i>B.H. Robinson</i>
B	29-Apr-2025	Final	Brigette Humphrey-Robinson Team Leader - Transport Planning & Advisory	<i>B.H. Robinson</i>
C	07-Jul-2025	Update to include HTP	Brigette Humphrey-Robinson Team Leader - Transport Planning & Advisory	<i>B.H. Robinson</i>

## Table of Contents

1.0	Introduction	1
1.1	Project overview	1
1.2	Purpose of this report	3
1.3	References	3
2.0	Existing environment	4
2.1	Site location	4
2.2	Existing road network	4
2.2.1	New England Highway	4
2.2.2	Hebden Road	5
2.3	Crash history	5
2.4	Existing traffic volumes	6
2.4.1	Traffic survey data	6
2.4.2	Average annual daily traffic volumes	9
2.5	Key intersection performance	9
2.6	Public transport	11
2.7	Active transport	11
3.0	Construction impact assessment	12
3.1	Construction program	12
3.2	Construction hours	12
3.3	Construction arrangements	12
3.3.1	Antienne STSS	12
3.3.2	Fibre optic route	13
3.3.3	Proposed Antienne STSS connections and rebuild of feeder 95U	13
3.4	Construction traffic volumes	14
3.5	Traffic distribution	14
3.6	Intersection performance	15
3.7	Site access arrangements	16
3.8	Mid-block road network performance	17
3.9	Emergency vehicles	17
3.10	Access for OSOM vehicles	17
3.11	Cumulative impact assessment	19
3.11.1	Sandy Creek STSS	19
3.11.2	The Liddell Future Land Use and Enabling Works Project	19
3.11.3	The Hunter Transmission Project	19
3.12	Mitigation and management measures	22
4.0	Operational impact assessment	23
5.0	Summary and conclusion	24
Appendix A		
	SIDRA INTERSECTION outputs	A

## 1.0 Introduction

AECOM Australia Pty Ltd (AECOM) has been engaged by Ausgrid to prepare a Traffic Impact Assessment (TIA) for the proposed Hunter Central Coast Renewable Energy Zone (HCC REZ) Network Infrastructure works at Muswellbrook, NSW (the Project).

### 1.1 Project overview

The Hunter-Central Coast Renewable Energy Zone (HCC REZ) was formally declared by the Minister for Energy and published in the NSW Gazette on 9 December 2022. As part of the NSW Government's clean energy transition, the REZ aims to deliver an additional one gigawatt (GW) of renewable energy transfer capacity by mid-2028. This would help provide consumers with cleaner, more affordable, and reliable electricity.

EnergyCo is responsible for developing and overseeing the planning and approval process for the REZ Infrastructure. EnergyCo selected Ausgrid as the preferred network operator for the REZ. Ausgrid would design, build, finance, operate and maintain the REZ infrastructure. Ausgrid's proposed solution involves a major augmentation of Ausgrid's electricity network in the Hunter region to provide an additional one GW of renewable energy transfer capacity by mid-2028. This would include works which span multiple Local Government Areas (LGAs), and comprising:

- Rebuilding sub-transmission lines
- Constructing two new substations
- Augmenting two existing substations.


This work would facilitate the connection and transfer of power generated from batteries, pumped hydro, solar, and wind farms to electricity consumers in the Muswellbrook and Newcastle areas.

The HCC REZ infrastructure would predominantly be constructed on land owned by Ausgrid or on public land. The sub transmission lines would be predominantly built within corridors of land known as sub transmission line easements. Ausgrid would use existing easements where possible; however, there would be the need to widen easements or acquire new easements in some sections.

The Project specifically includes network infrastructure works in the Hebden Road area within the Muswellbrook Shire LGA, including the following:

- New sub transmission switching station known as Antienne STSS located at Lot 9 DP250890 Hebden Road, Muswellbrook (as shown in Figure 1-1)
- Overhead connection works to existing network (as shown in Figure 1-2)
- Rebuild of the feeder 95U to southeast of new Antienne STSS (as shown in Figure 1-2)
- Optic fibre cable installation along Hebden Road and then north under 95U feeder towards Muswellbrook (as shown in Figure 1-3).



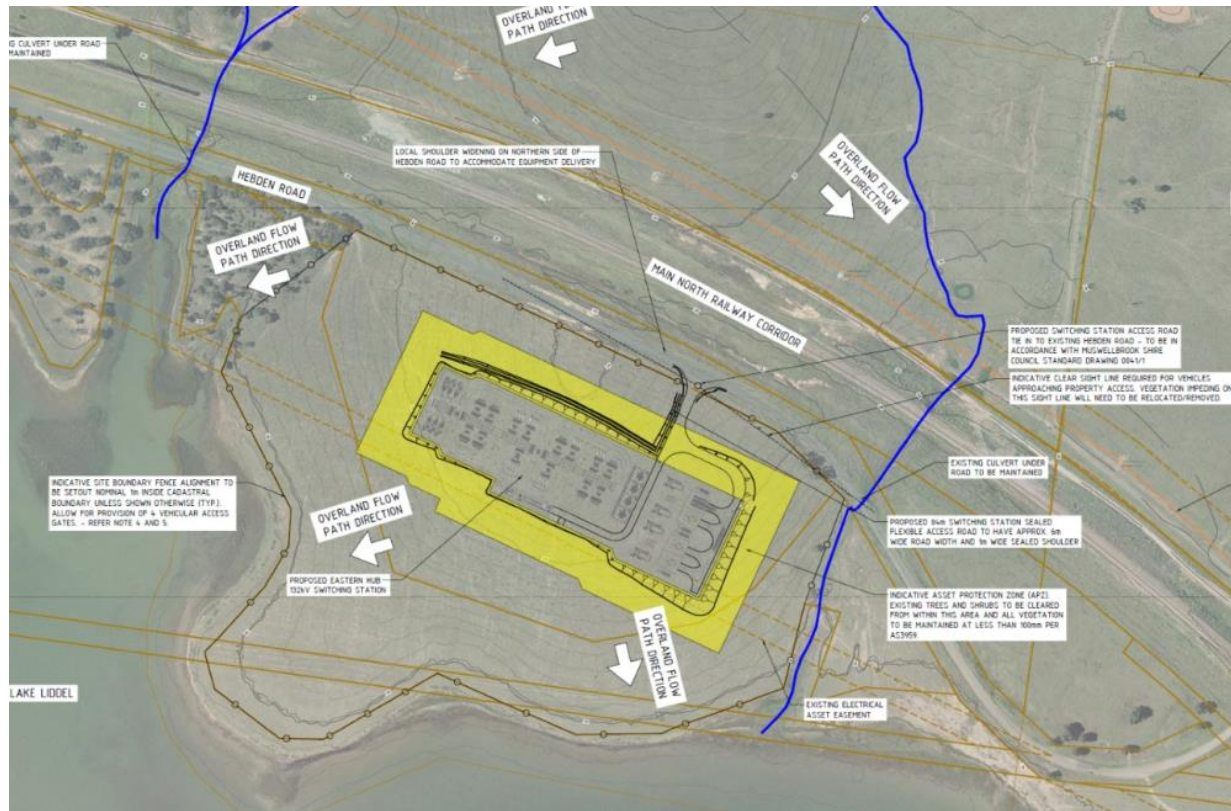

Source: Ausgrid

**Figure 1-1 Proposed Antienne STSS**

Source: Ausgrid

**Figure 1-2 Proposed Antienne STSS connections and rebuild of feeder 95U**





Source: Ausgrid

**Figure 1-3 Fibre optic route**

## 1.2 Purpose of this report

This TIA provides an assessment of the potential traffic impacts associated with the Project, including consideration of the following:

- Existing traffic and transport conditions in the Project area
- Traffic generating characteristics of the Project during construction and operation
- Likely routes to be used for oversize/overmass (OSOM) deliveries
- Traffic impacts during construction and operation of the Project and cumulative impacts with the proposed Hunter Transmission Project
- Suitability of the proposed site access arrangements
- Mitigation measures, if required, to minimise the traffic impacts of the Project.

## 1.3 References

In preparing this TIA, references have been made to the following documents and datasets:

- Transport for New South Wales (TfNSW) Open Data for NSW Crash data
- TfNSW National Heavy Vehicle Regulator (NHVR) National Network Map
- Interim Construction Noise Guideline (Department of Environment and Climate Change NSW, 2009)
- Austroads Guide to Traffic Management Part 6: Intersections, Interchanges and Crossings
- TfNSW Guide To Transport Impact Assessment, 20123
- TfNSW Traffic Modelling Guidelines, 2013
- Other documents and datasets, as referenced in this report.




## 2.0 Existing environment

### 2.1 Site location

The Project area is located in Hebden, within the Muswellbrook Shire LGA in the Upper Hunter region. The project area is situated around 30 kilometres northwest of Singleton and 12.5 kilometres southeast of Muswellbrook. The location of the Project area is shown in Figure 2-1.

Lake Liddell and a coal unloader facility in the south, the Hunter Line towards the north-east, and recreational parks on the west side of the Antienne STSS site bound the Project area. Several coal mine sites and substation sites surround the outer extents of the Project area.

Under the *Muswellbrook Local Environmental Plan 2009* (LEP), the Antienne site is zoned as Public Recreation (RE1) and is surrounded by zoned Infrastructure (SP2) on the west and south sides, and zoned Primary Production (RU1) on the north and east side.

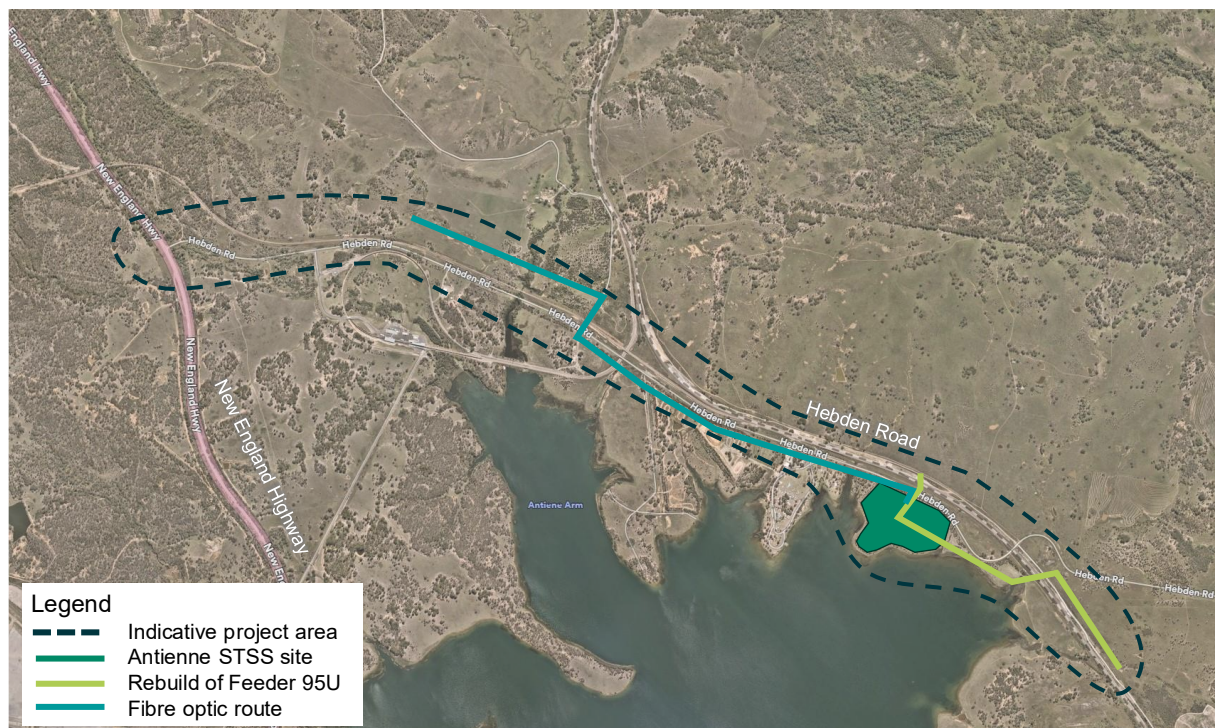

Basemap source: Nearmap, image taken 14 March 2025

**Figure 2-1 Project area**

### 2.2 Existing road network

Key roads near the Project area include the New England Highway and Hebden Road.

#### 2.2.1 New England Highway

New England Highway is classified as a State highway that is 883 kilometres long and spans from Newcastle to Yarraman in Queensland. The New England Highway runs in a north-south direction west of the Project area. The New England Highway provides an undivided carriageway, allowing for two lanes of travel in the northbound direction and a single lane in the southbound direction in the vicinity of the Project area.

The posted speed limit on the New England Highway is 100 kilometres per hour for vehicles near the Project area.

### 2.2.2 Hebden Road

Hebden Road is a rural road that intersects with the New England Highway to the north and south of the Project area. It provides an undivided carriageway with one lane in each direction. The posted speed limit on Hebden Road is 80 kilometres per hour near the Project area.

The Project area is most commonly accessed via the unsignalised intersection of the New England Highway and Hebden Road to the north. Auxiliary turn lanes are provided at the New England Highway and Hebden Road for the left turn and right turn into Hebden Road.

Hebden Road is narrow in sections, and it may be difficult for two heavy vehicles to pass each other while travelling close to the posted speed limit of 80 kilometres, representing safety concerns.

## 2.3 Crash history

The most recent five years of available crash data within the Project area were obtained from Transport's Centre for Road Safety (2019 to 2023), as shown in Figure 2-2.

Five crashes occurred within the Project area. One occurred on Hebden Road, involving a vehicle driving off the path into an object and resulting in a serious injury. The other four crashes occurred on New England Highway near the intersection of the New England Highway and Hebden Road, resulting in one minor injury and three non-casualty injuries.



Source: <https://opendata.transport.nsw.gov.au/dataset/nsw-crash-data>, accessed March 2025

Figure 2-2 Crash severity

## **2.4 Existing traffic volumes**

### **2.4.1 Traffic survey data**

Two types of traffic survey data were collected and analysed to better understand the existing traffic volumes within the Project area. They include:

- Classified intersection counts at the key intersection of the New England Highway and Hebden Road (to the west of the Project area) were conducted on Thursday, 3 April 2025, during the typical weekday peak periods.
- Seven-day automatic traffic counts on Hebden Road within the Project area between Wednesday, 2 April 2025, and Tuesday, 8 April 2025.


#### **2.4.1.1 Classified intersection count data**

The classified intersection counts indicated that the weekday peak hours at the intersection of the New England Highway and Hebden Road are:

- AM Peak hour: 6:15am to 7:15am
- PM Peak hour: 4:30pm to 5:30pm.

The turning movements at the intersection of the New England Highway and Hebden Road during the weekday AM and PM peak hours are shown in Figure 2-3.



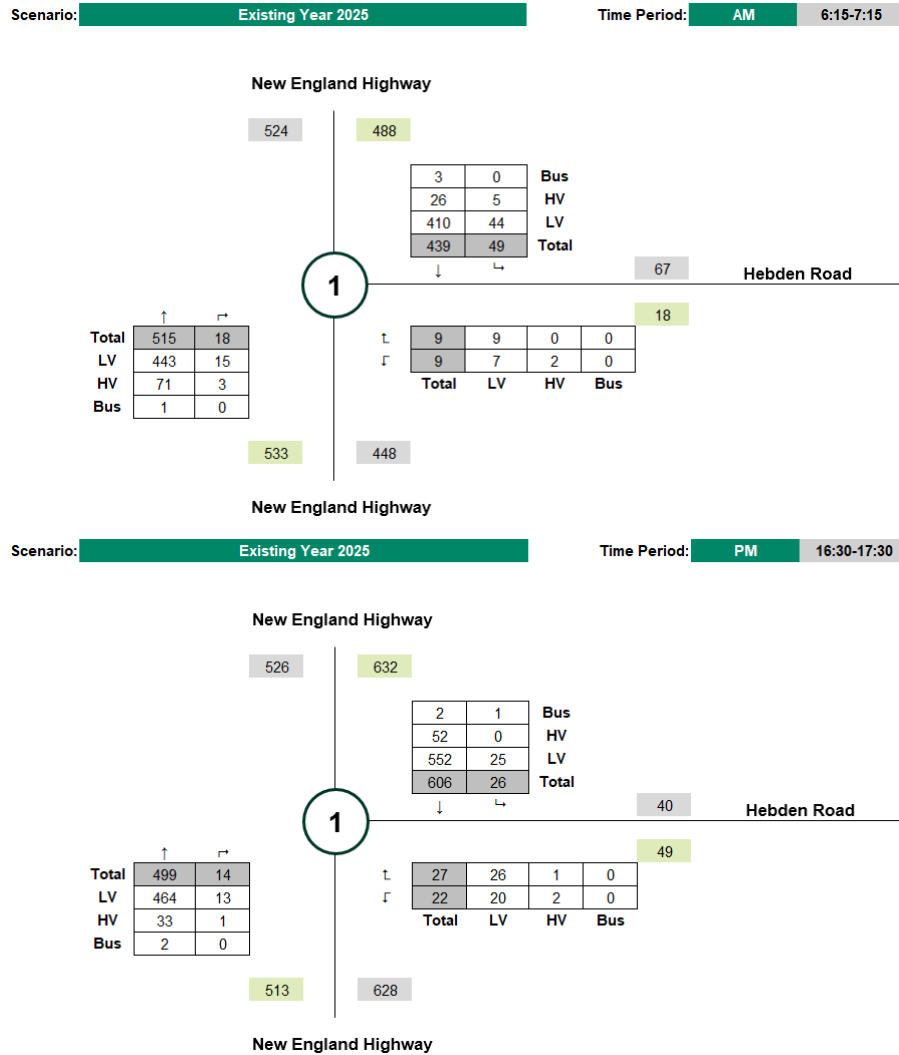

**Figure 2-3 Existing 2025 intersection volumes**

A site visit was also conducted during the PM peak period on Thursday, 3 April 2025. During the site visit, moderate traffic was observed in the northbound and southbound directions on the New England Highway with no vehicle queuing observed at the New England Highway and Hebden Road intersection.

### 2.4.1.2 Mid-block traffic count data

The seven day automatic traffic counter was located to the west of the proposed Antienne STSS site, as shown in Figure 2-4.



Source: Nearmap, image taken 14 March 2025

**Figure 2-4 Tube count location**

A summary of the two-way weekday traffic profile is displayed in Figure 2-5. The highest daily traffic volumes occurred on Thursday, with around 390 vehicles recorded throughout the day. The daily weekday traffic profile indicates the following:

- AM peak hour occurred at 5:00am with around 60 two-way vehicles movements and an 85:15 eastbound: westbound split.
- PM peak hour occurred at 5:00pm with around 40 two-way vehicle movements and a 32:68 eastbound: westbound split.

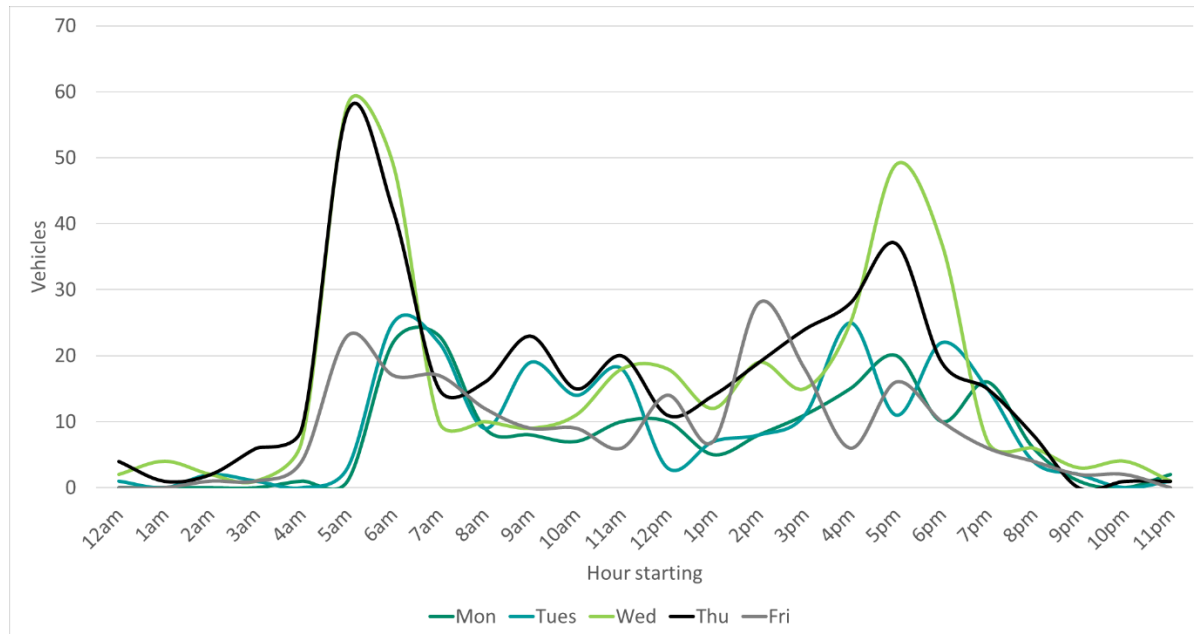


Figure 2-5 Daily weekday traffic profile

#### 2.4.2 Average annual daily traffic volumes

Traffic volumes were sourced from the TfNSW historical traffic volume viewer for the permanent classifier (Station ID 6154) located on the New England Highway, 5.2 kilometres north of the Project area. The annual average daily traffic (AADT) volumes between 2015 and 2022, along with the corresponding compound annual traffic growth rate across this period are summarised in Table 2-1. Overall, traffic volumes on the New England Highway have been reducing since 2019.

Table 2-1 Historical AADT traffic volumes on and growth rates

Direction	Annual average daily traffic (AADT)								Average annual compound annual growth (2015-2022)
	2015	2016	2017	2018	2019	2020	2021	2022	
Northbound	4,620	4,576	4,632	4,654	4,762	4,337	4,439	4,207	-1.3%
Southbound	4,713	4,626	4,694	4,710	4,808	4,372	4,446	4,307	-1.3%
<b>Total</b>	<b>9,333</b>	<b>9,202</b>	<b>9,326</b>	<b>9,364</b>	<b>9,570</b>	<b>8,709</b>	<b>8,885</b>	<b>8,514</b>	<b>-1.3%</b>

Based on this analysis no traffic growth has been adopted in this assessment, and the existing surveyed 2025 traffic volumes are considered representative of traffic volumes throughout the construction period, which is anticipated to commence in January 2026.

## 2.5 Key intersection performance

The weekday AM and PM peak hour operation of the New England Highway and Hebden Road intersection was assessed using the SIDRA INTERSECTION 9.1 software, adopting the surveyed traffic volumes and site observations. SIDRA INTERSECTION is a micro-analytical modelling software package, capable of analysing isolated and coordinated intersections. The key outputs from SIDRA INTERSECTION are summarised in Table 2-2.



**Table 2-2 SIDRA INTERSECTION modelling outputs**

Output	Description
Degree of saturation (DoS)	Ratio of the arrival (demand) flow rate to the capacity of the approach or intersection during a given flow period. Where DoS is close to 1.00, the traffic demand is effectively equal to the capacity of the approach or intersection
95th percentile vehicle queue (metres)	A statistical value which represents the queuing experienced on an approach to an intersection
Average delay (seconds) and level of service (LoS)	Average delay is commonly used to assess the operational performance of intersections, with LoS used as an index.

A summary of the intersection LoS criteria is shown in Table 2-3. Common practice suggests that when intersection performance falls to LoS D, investigations should be initiated to determine if suitable remediation can be provided.

**Table 2-3 LoS criteria for intersections**

LoS	Average delay per vehicle (seconds per vehicle)	Traffic signals and roundabouts	Give way and stop sign
A	Less than 14	Good operation	Good operation
B	15 to 28	Good with acceptable delays and spare capacity	Acceptable delays and spare capacity
C	29 to 42	Satisfactory	Satisfactory, but accident study required
D	43 to 56	Operating near capacity	Near capacity and accident study required
E	57 to 70	At capacity, at signals incidents will cause excessive delays	At capacity, requires other control mode
F	Greater than 70	Extra capacity required	Extreme delay, major treatment required

Source: Traffic Modelling Guidelines, Transport, 2013.

It is noted that the critical movement for LoS at a roundabout or priority-controlled intersection is the movement with the worst delay, whereas for a signalised intersection, the average delay over all movements is adopted.

Table 2-4 summarises the existing intersection operation of the New England Highway and Hebden Road intersection during weekday AM and PM peak hours.

**Table 2-4 Existing intersection performance**

Intersection	Peak hour	DoS	Average delays (seconds)	95th percentile queue (metres)	Level of service (LoS)
New England Highway and Hebden Road	AM	0.058	27	1.2	B
	PM	0.284	46	6.0	D

The New England Highway and Hebden Road intersection currently operates well at a LOS B during AM peak hour and satisfactorily at a LOS D during the PM peak hour. There is minimal vehicle queuing on all approaches to the intersection. However, the model indicates that vehicles turning right from Hebden Road to the New England Highway experience some delays, particularly during the PM peak hour. This is consistent with on-site observations, which indicated minimal vehicle queues occurred during the weekday peak hours.

## **2.6 Public transport**

The Hunter line passes by northeast of the Project area and stops at Muswellbrook train station, approximately 14 kilometres north-west of the Project area.

## **2.7 Active transport**

No pedestrian or cycling infrastructure is currently provided within the Project area. This reflects the predominantly surrounding area, which consists of primary production and industrial land uses.

## 3.0 Construction impact assessment

### 3.1 Construction program

The Project's construction would commence in early 2026 and take approximately 24 months to complete. However, this timing may change depending on market demand.

The Project's construction would involve three activities as summarised in Table 3-1, with further details discussed in Section 3.3.

**Table 3-1 Construction timelines**

Construction activity	Indicative timelines
Antienne STSS	January 2026 to mid-2027
Optic fibre cable installation	December 2025 to mid-2027
Rebuild of the feeder 95U to southeast of new Antienne STSS and Antienne STSS connections	January 2026 to mid-2026

### 3.2 Construction hours

Construction would be undertaken generally in accordance with the *Interim Construction Noise Guideline* (Department of Environment and Climate Change NSW, 2009), with extended hours of work on weekends and NSW public holidays. Construction hours would generally be limited to:

- Monday-Saturday: 7:00 am to 6:00 pm
- No work on Sundays or public holidays.


### 3.3 Construction arrangements

#### 3.3.1 Antienne STSS

Construction at the Antienne site involves building a new substation, with access provided via a new intersection along Hebden Road, just east of the Lake Liddell Recreation Area. A car park, approximately 60 metres by 20 metres (see Figure 3-1), would be built on the west side of the Hebden Road access and would also serve as a lay-down and delivery area.

The busiest period for construction vehicle traffic is expected to occur on concrete pour days, which may take place on up to five days throughout the construction period and involve up to 30–40 light vehicles and 40 heavy vehicles per day (assumed to be one-way vehicle movements). OSOM vehicle use would include around 8 to 13 low loaders transporting the control room and heavy machinery such as excavators, oversized cranes, and a dozer, with no more than one of these vehicle movements likely to occur at the same time.



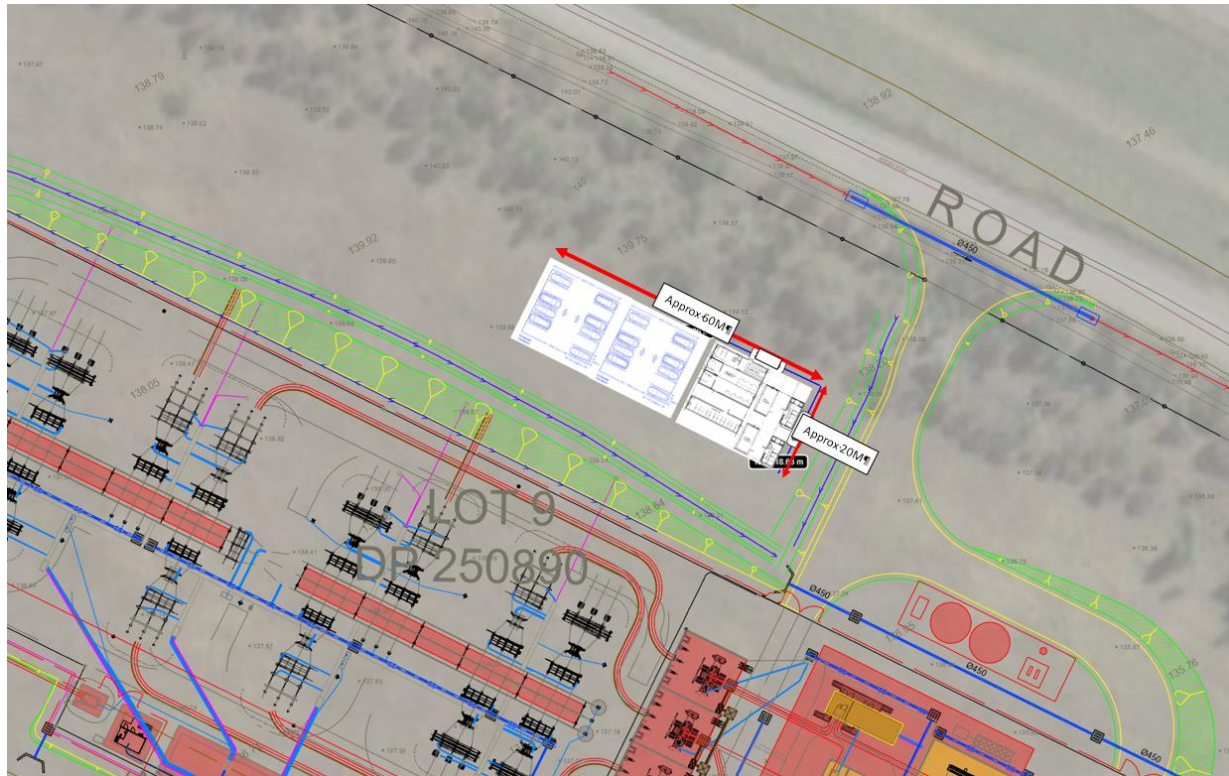

Source: Ausgrid

**Figure 3-1 Proposed site access, car park and lay-down area**

### 3.3.2 Fibre optic route

Fibre optic installation activities involve laying fibre optic cables along the south side of Hebden Road from the Antienne STSS site to Antienne Railway Station Road, as well as along the north side of Hebden Road and under the 95U Feeder towards Muswellbrook.

Multiple work sites would be established along Hebden Road to complete the installation. Construction workers would either set up on the roadside or park at the main site where safety concerns arise. The construction vehicle fleet for these works would include five light vehicles and two heavy vehicles per day, with low loaders for delivering machinery.

### 3.3.3 Proposed Antienne STSS connections and rebuild of feeder 95U

The proposed works for the rebuild of Feeder 95U and the Antienne STSS connection would take place north of the railway track, transitioning to the Antienne STSS connection.

Construction workers would access the area via Hebden Road and park near the structures being worked on. During peak construction activities, the vehicle fleet would include seven to 10 light vehicles and eight heavy vehicles, with approximately 15 to 20 workers on site on any day.

OSOM vehicle requirements would include a 100-tonne and 60-tonne crane, a 50-metre elevated work platform (EWP) vehicle, a drill rig, and a semi-trailer with a quad float.

### 3.4 Construction traffic volumes

The peak construction traffic volumes would occur when the construction of the Antienne STSS and the fibre optic route would overlap. At this time, no construction vehicles are expected to be generated by the works for the rebuild of feeder 95U and Antienne STSS connections.

Across the two sites, construction is expected to generate approximately 90 light vehicle movements (two-way) and 84 heavy vehicle movements (two-way), totalling 174 vehicle movements (two-way) per day. For the purpose of this conservative assessment, construction traffic for the fibre optic construction works are assumed to also access the Antienne STSS site.

The construction trip generation during the road network peak hours is summarised in Table 3-2 and is based on the following assumptions:

- All light vehicles are expected to arrive during the road network's AM peak hour
- As the road network's PM peak hour occurs within construction hours, it is assumed that workers would not depart until after 6:00pm. Therefore, no light vehicle movements are anticipated during the road network's PM peak hour
- Heavy vehicles are expected to arrive steadily throughout the 11-hour working day, averaging 10 heavy vehicle movements per hour (two-way).


**Table 3-2 Construction traffic volumes**

Vehicle type	Peak hourly traffic volumes (trips/hr)					
	AM peak hour (6:15am to 7:15am)		PM peak hour (4:30-5:30pm)		Construction worker departure (6:00-7:00pm)	
	Inbound	Outbound	Inbound	Outbound	Inbound	Outbound
Light vehicles	45	0	0	0	0	45
Heavy vehicles	5	5	5	5	5	5
<b>Total</b>	<b>50</b>	<b>5</b>	<b>5</b>	<b>5</b>	<b>5</b>	<b>50</b>

It is noted that the traffic volumes at the intersection of the New England Highway and Hebden Road at 6:00pm are about 30% less than during the PM peak hour.

### 3.5 Traffic distribution

All construction traffic would travel to and from the New England Highway to access the construction sites via Hebden Road. Based on the 2025 intersection count data, the distribution of construction traffic was determined using the proportion of turning movement volumes at the intersection of the New England Highway and Hebden Road. The analysis indicates that 70% of construction traffic would approach from or depart to the north, and 30% to/from the south, as shown in Figure 3-2.

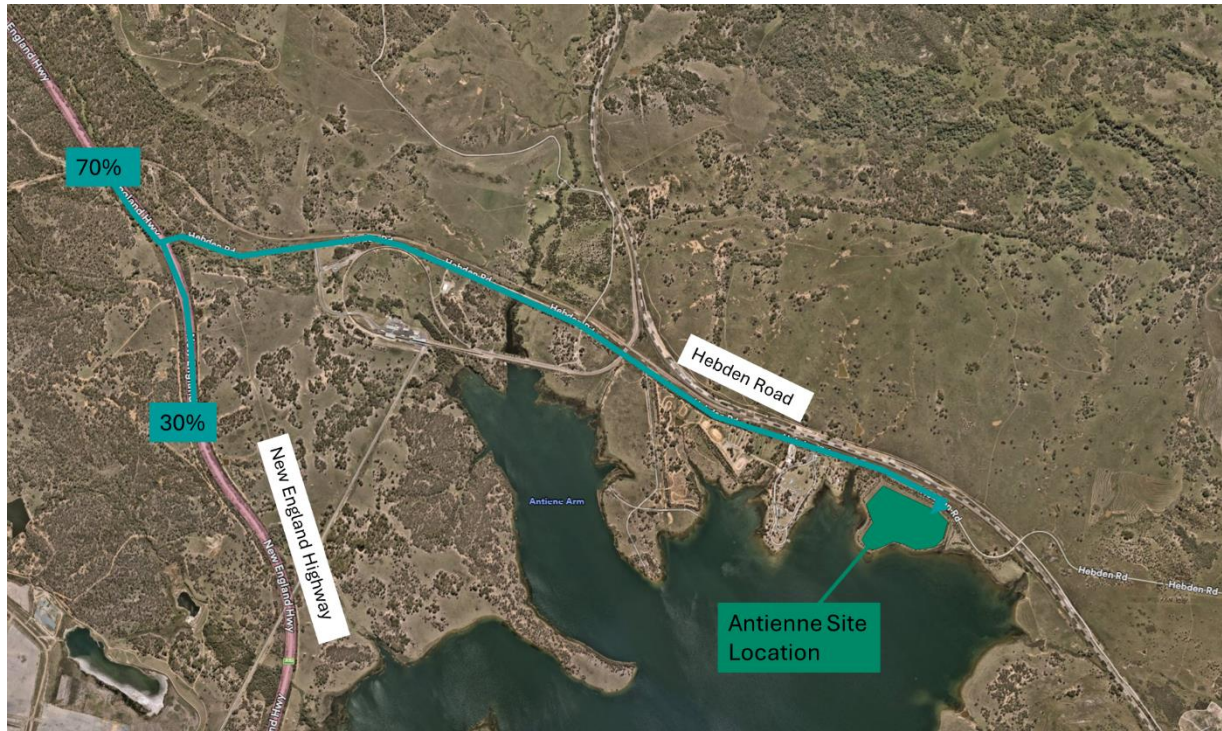

Source: Nearmap, image taken 14 March 2025

**Figure 3-2 Construction traffic distribution**

### 3.6 Intersection performance

The performance of the New England Highway and Hebden Road intersection has been assessed using the SIDRA INTERSECTION modelling software for the following scenarios:

- Road network AM and PM peak hour (refer to Table 3-3)
- Construction PM peak hour at 6:00pm to 7:00pm (refer to Table 3-4)

**Table 3-3 Intersection performance with construction traffic during the weekday AM and PM peak hours**

Intersection	Peak hour	Degree of Saturation (DoS)	Average delays (seconds)	95th percentile queue (metres)	Level of Service (LoS)
New England Highway and Hebden Road	AM	0.18	53	4	D
	PM	0.47	71	10	F
Proposed site access and Hebden Road	AM	0.07	7	2	A
	PM	0.03	9	1	A

Table 3-3 indicates that in the AM peak hour, the performance of the New England Highway and Hebden Road intersection would degrade slightly from LoS B to LOS D, with an increase in delay of 25 seconds and an additional two metres of queuing. In the PM peak hour, the performance is anticipated



to degrade from LoS D to LoS F, with an increase in delay of 24 seconds. The LoS F performance is associated with the eastbound right-turn movement from Hebden Road onto the New England Highway. This degradation occurs due to the high northbound and southbound traffic volumes on the New England Highway, which significantly reduce acceptable gaps for right-turning vehicles from Hebden Road. Notably, the LoS F is triggered by the presence of only five additional vehicles, as the delay experienced by each vehicle increases rapidly under these constrained conditions.

The proposed site access would operate with a LoS A during both the AM and PM peak hours.

Table 3-4 indicates that the New England Highway and Hebden Road intersection would operate well at LOS B with and without the construction vehicles at 6:00pm.


**Table 3-4 Construction intersection performance at 6:00pm**

Intersection	Scenario	Degree of Saturation (DoS)	Average delays (seconds)	95th percentile queue (metres)	Level of Service (LoS)
New England Highway and Hebden Road	Without construction	0.11	20	3	B
	With construction	0.30	25	8	B
Proposed site access and Hebden Road	With construction	0.02	9	1	A

### 3.7 Site access arrangements

Austrroads Guide to Traffic Management Part 6: Intersections, Interchanges and Crossings Management provides warrants for the preferred minimum turn treatments for major roads. Turn treatments for intersections are typically determined based on vehicle speeds and the relationship between through traffic volumes and turning volumes on the major road. Possible turn treatments include basic (BA), auxiliary lane (AU) and channelised (CH) turn treatments.

Figure 3-3 has been prepared to assess the anticipated turning traffic movements at the site access on Hebden Road during the construction stage of the Project against the Austrroads turn treatment warrants. The assessment only considers the warrants for the eastbound right turn treatment into the Antienne STSS site as no construction vehicles are expected to turn left into the site. As a conservative approach, it is assumed all 55 construction vehicles would enter the Antienne STSS site for the warrant assessment.

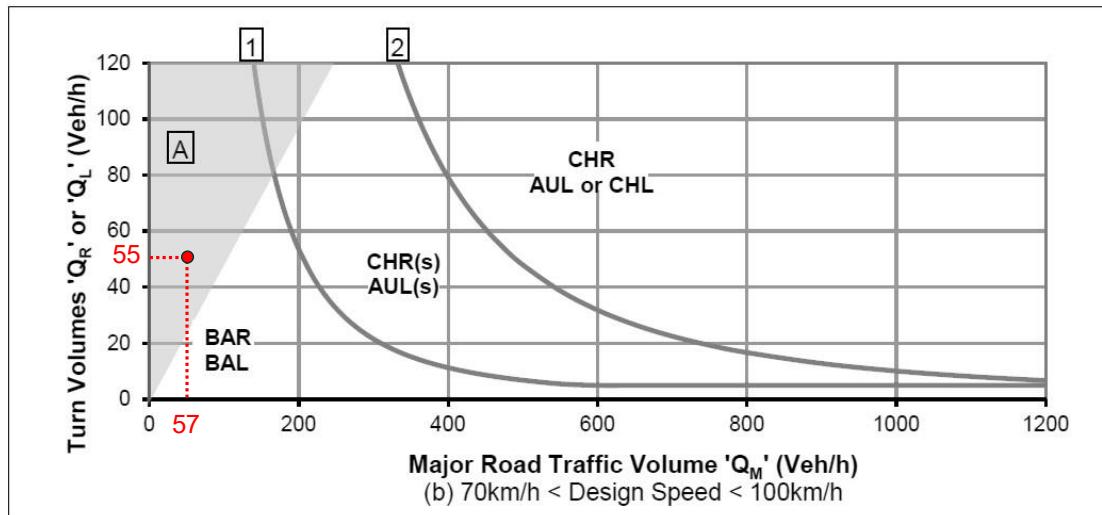

Source: Figure 3.25 of Guide to Traffic Management Part 6: Intersections, Interchanges and Crossings Management

**Figure 3-3 Warrants for turn treatments on lower speed rural roads at unsignalised intersections**

The warrants assessment suggests a BA right turn treatment is an appropriate turn treatment on Hebden Road into the construction site access. Therefore, channelised turn treatments are not required.

### 3.8 Mid-block road network performance

Based on Austroads guidance, it is estimated that the mid-block lane capacity of Hebden Road is approximately 800 vehicles per hour in each direction. Mid-block traffic volumes on Hebden Road are expected to reach up to 105 vehicles per hour (two-way) in the weekday peak hours during construction of the proposal. Therefore, Hebden Road is anticipated to operate with considerable spare capacity.

Stop-go traffic control on Hebden Road would be required to facilitate the construction of the access road to the Antienne STSS site, and for approximately 8 weeks during construction hours to accommodate the fibre optic installation. It is estimated that the temporary stop-go conditions, which are expected to include a short section of two-way one-lane arrangements, would typically result in only minor vehicle delays and queuing on Hebden Road. Nevertheless, temporary stop-go conditions should be minimised as much as possible to maintain the existing capacity of Hebden Road and minimise vehicle delays and queuing.

### 3.9 Emergency vehicles


Hebden Road and New England Highway are currently used by emergency services. Construction activities may require temporary stop-go traffic control. However, no full road closures are expected. As such, emergency vehicle access would be maintained through the Project area during construction. Emergency protocols on the site would include a requirement for traffic controllers to assist with emergency access through the Project area should any temporary traffic modifications be in place.

### 3.10 Access for OSOM vehicles

The current OSOM network surrounding the Project area has been reviewed to assess accessibility and available routes for transporting oversize and larger loads to the three construction sites. Figure 3-4 displays the surrounding NHVR approved and restricted roads. Hebden Road is not an approved NHVR route and will require NHVR permits. Several key corridors would be accessible under restricted conditions (shown in yellow in Figure 3-4) including:

- Maitland Road, New England Highway and John Renshaw Drive between Sparkle Street and Pacific Motorway

- Prior to travel on the Pacific Highway at Hexham, the operator must contact the Hexham Straight Widening Project on 1800 515 141 a minimum of five (5) days prior to your proposed commencement date. Failure to provide notice may result in delays to travel.
- Prior to travel on the Pacific Highway, New England Highway and Pacific Motorway between Tomago, Tarro and Lenaghan, the operator must contact the Black Hill to Tomago Project on 1800 094 895 a minimum of five (5) days prior to your proposed commencement date. Failure to provide notice may result in delays to travel.
- Hunter Express between John Renshaw Drive to New England Highway
  - Vehicles or combinations exceeding 3.2 metres wide are not permitted to travel from Monday to Friday from 5:00am to 9:00am and from Monday to Friday from 4:00pm to 6:00pm (except on state-wide public holidays).
- New England Highway between Hunter Express to Magpie Street
  - Vehicles or combinations exceeding 3.2 metres wide are not permitted to travel from Monday to Friday from 5:00am to 9:00am and from Monday to Friday from 3:00pm to 6:00pm (except on state-wide public holidays).

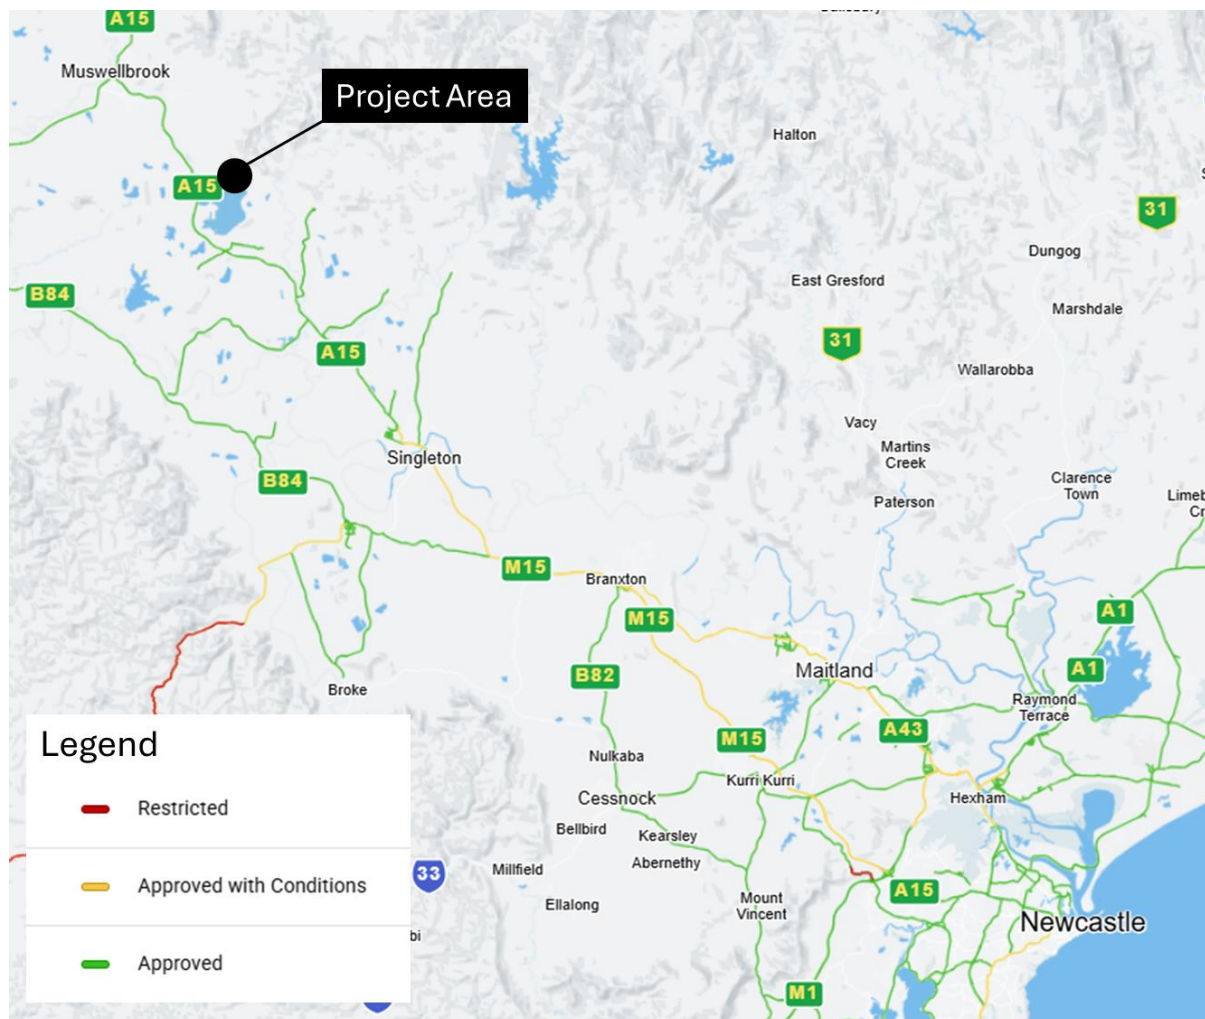

Source: [https://maps.nhvr.gov.au/?networkLayerContext=NATIONAL\\_MAP&view=Category&exemptionSetId=-2&networkIds=%5B2157%5D](https://maps.nhvr.gov.au/?networkLayerContext=NATIONAL_MAP&view=Category&exemptionSetId=-2&networkIds=%5B2157%5D), accessed April 2025

Figure 3-4 NHVR approved OSOM routes surrounding the Project area

### 3.11 Cumulative impact assessment

The Project area is located within close proximity to three nearby projects, including:

- Sandy Creek STSS
- The Liddell Future Land Use and Enabling Works Project
- The Hunter Transmission Project (HTP).

The cumulative impacts associated these projects are discussed the following sections.

#### 3.11.1 Sandy Creek STSS

The Sandy Creek STSS, located to the north of Muswellbrook, would be constructed on behalf of Ausgrid concurrently with the Project. However, the peak construction activity (i.e. the concrete pour days) would be staggered between the two sites. This approach would minimise cumulative impacts, as one site would be relatively quiet while the other is undertaking peak activity.

#### 3.11.2 The Liddell Future Land Use and Enabling Works Project

The Liddell Future Land Use and Enabling Works Project aims to transition towards a low-carbon future by closing its coal-fired power station. The State Government approved AGL's plan to convert the Liddell site into a renewable energy hub in early 2025. Remediation works have been progressing and would continue throughout the Project's construction period. Therefore, the traffic generated from the remediation works have been accounted for in the 2025 traffic survey data and it is not expected that there are any cumulative impacts associated with the Project.

#### 3.11.3 The Hunter Transmission Project

The HTP is a critical State significant infrastructure project that would construct a new above-ground 500 kilovolt (kV) transmission line of around 100 kilometres between Bayswater in the Upper Hunter and Olney in the Lower Hunter, connecting the existing transmission lines already operated by Transgrid. HTP is one of the State's most critical energy projects and would provide clean and reliable electricity for consumers for at least 50 years.

According to the HTP fact sheet released by EnergyCo in Mar 2025<sup>1</sup>, three temporary construction support sites would support the HTP construction and would provide workforce accommodation, laydown areas, parking, amenities, and stage the transport of equipment during the construction period.

One of the HTP construction support sites is planned along Hebden Road between the intersection of the New England Highway and Hebden Road and the proposed access to the Antienne STSS site on Hebden Road, as shown in Figure 3-5. This temporary construction support site would remain operational for the full duration of the HTP construction period and be removed once the HTP construction concludes.

The HTP construction support site on Hebden Road is anticipated to generate up to 434 light vehicle movement (two-way) and 409 heavy vehicle movements (two-way) on Hebden Road per day. All traffic is expected to use the intersection of the New England Highway and Hebden Road to access the support site.

The estimated trip generation during the road network peak hours is shown in Table 3-5 and is based on the following assumptions:


- All light vehicles are expected to depart the HTP construction support site during the road network's AM peak hour (6:15am to 7:15am).
- As the road network's PM peak hour (4:30pm to 5:30pm) occurs within the standard construction hours (7:00pm to 6:00pm), it is assumed that workers would not depart the HTP main construction site until after 6:00pm. Therefore, no light vehicle movements are anticipated during the road network's PM peak hour.

---

<sup>1</sup> EnergyCo, Construction support sites - HTP Environment Impact Statement, March 2025  
[https://aecomaus.sharepoint.com/sites/ProjectsFolder-TransportAdvisory-60751984HCCREZ/Shared Documents/60751984 HCC REZ/400\\_Technical/431\\_TechnicalArea\\_TIA/20250707-60751984 HCC REZ Hebden TIA \(Rev C\).docx](https://aecomaus.sharepoint.com/sites/ProjectsFolder-TransportAdvisory-60751984HCCREZ/Shared Documents/60751984 HCC REZ/400_Technical/431_TechnicalArea_TIA/20250707-60751984 HCC REZ Hebden TIA (Rev C).docx)  
Revision C – 07-Jul-2025  
Prepared for – Ausgrid – ABN: 20 093 846 925



- Heavy vehicles are expected to arrive and depart steadily throughout the 11-hour working day, averaging 38 heavy vehicle movements per hour (two-way).

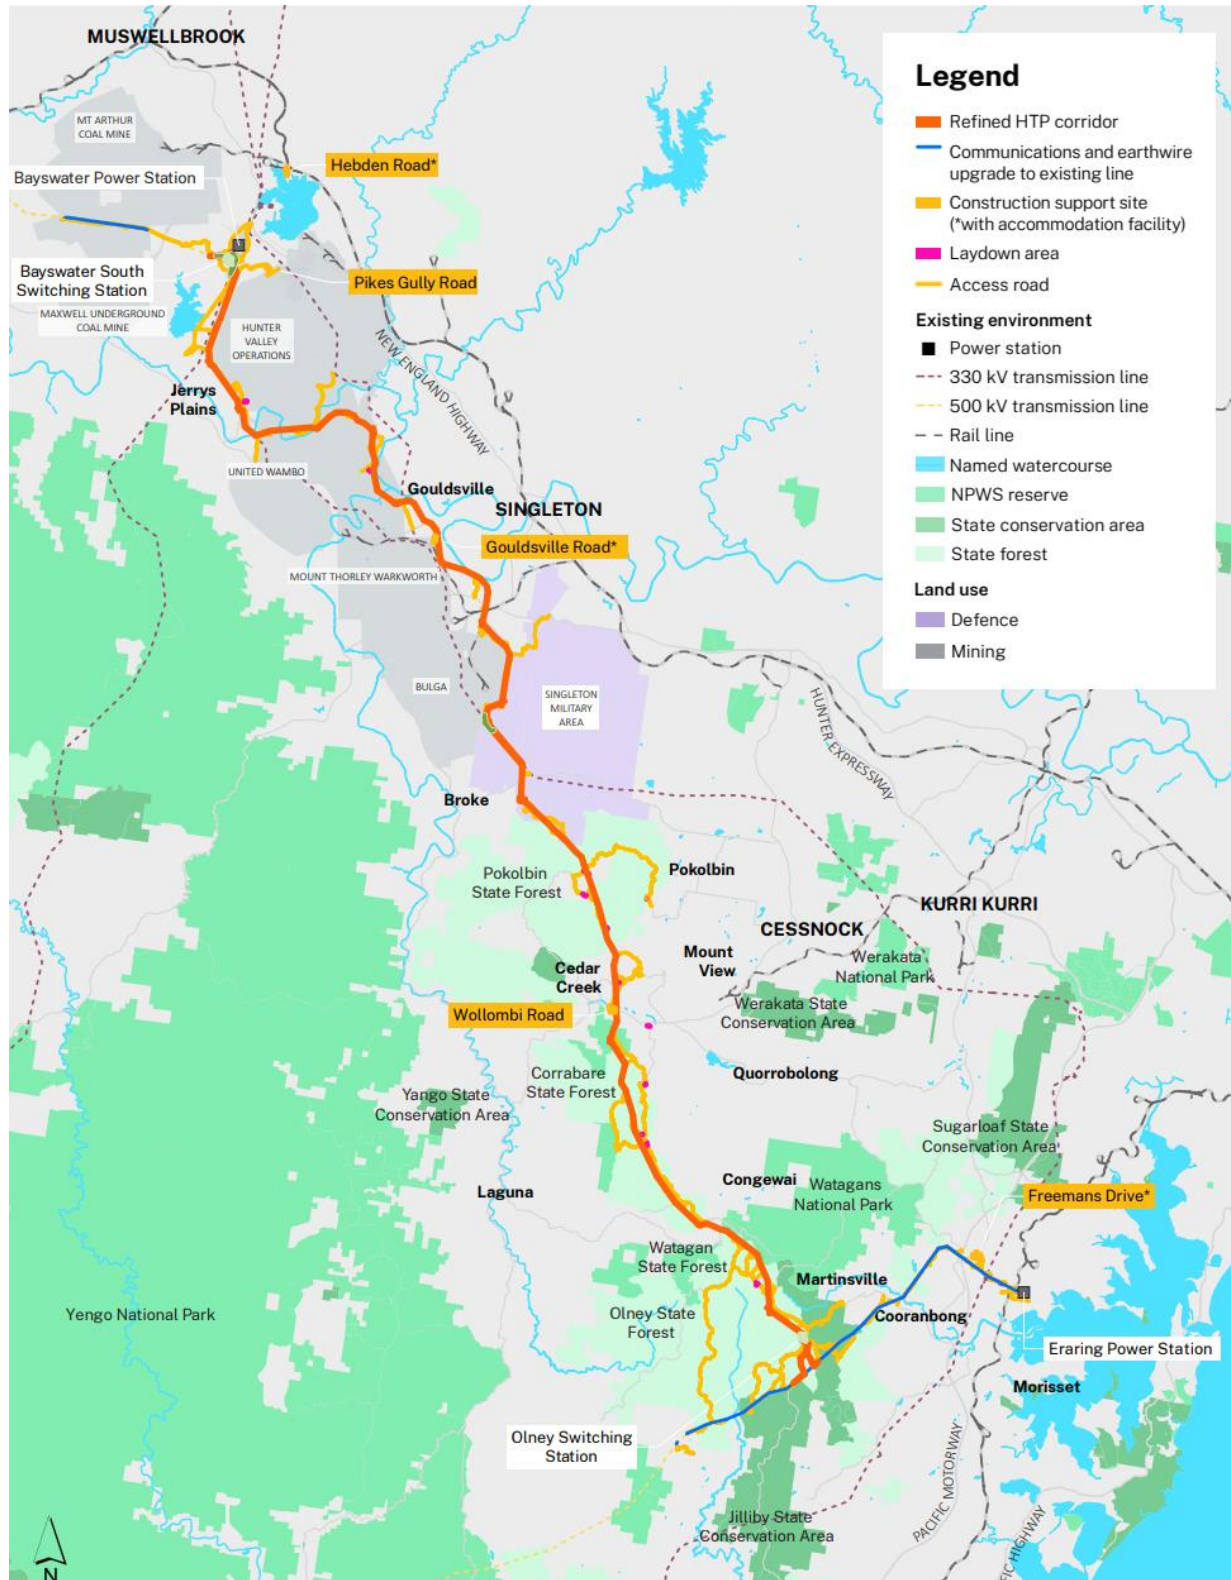

Source: HTP fact sheet released, EnergyCo March 2025

**Figure 3-5 HTP - Transport routes and construction support sites**

**Table 3-5 HTP construction support site – peak traffic volumes**

Vehicle type	Peak hourly traffic volumes (trips/hr)					
	AM peak hour (6:15am to 7:15am)		PM peak hour (4:30-5:30pm)		Project's construction worker departure hour (6:00-7:00pm)	
	Inbound	Outbound	Inbound	Outbound	Inbound	Outbound
Light vehicles	0	217	0	0	217	0
Heavy vehicles	19	19	19	19	19	19
<b>Total</b>	<b>19</b>	<b>236</b>	<b>19</b>	<b>19</b>	<b>236</b>	<b>19</b>

Construction works for the HTP are proposed to commence in 2027, with operations expected to begin by late 2029. Therefore, the start of the HTP construction could potentially overlap with the end of the Project's construction. As the start and the end of a construction period are typically associated with low traffic movements, the cumulative traffic impacts are anticipated to be minimal.

Notwithstanding this, for the purpose of this study, a conservative approach has been adopted to assess the impacts if the peak HTP construction activities coincided with the Project's peak construction period. SIDRA INTERSECTION modelling of the New England Highway and Hebden Road intersection has been undertaken to assess the cumulative impacts of both the Project's construction and the HTP construction.

A comparison of the SIDRA INTERSECTION modelling results for the cumulative assessment is shown in Table 3-6, indicating the following key findings:

- AM peak hour: although the LoS at the New England Highway and Hebden Road intersection would change from D to E, the increase in average delays would be minimal (approximately 5 seconds)
- PM peak hour: the LoS at the New England Highway and Hebden Road intersection would remain at F with an increase in average delays of 8 seconds
- The Project's construction worker departure hour: vehicle delays at the New England Highway and Hebden Road intersection would increase by 23 seconds and the LoS would change from B to D. However, the increase in vehicle queuing would be minimal at only 6 metres, equivalent to approximately one light vehicle.

Overall, the conservative assessment indicates that cumulative impacts of Project and the HTP construction support site on Hebden Road would cause a minor increase to vehicle delays at the New England Highway and Hebden Road intersection during the peak hours. However, it is anticipated that this impact would be minimised if the start of the HTP construction would overlap with the end of the Project's construction, as is currently planned.

**Table 3-6 Intersection performance with HTP construction traffic – New England Highway and Hebden Road**

Peak hour	Scenario	Degree of Saturation (DoS)	Average delays (seconds)	95th percentile queue (metres)	Level of Service (LoS)
AM peak (6:15am to 7:15am)	With Project	0.18	53	4	D
	With cumulative impacts (HTP)	0.19	58	4	E
PM peak (4:30pm to 5:30pm)	With Project	0.47	71	10	F
	With cumulative impacts (HTP)	0.51	79	11	F
Construction worker departure (6:00pm to 7:00pm)	With Project	0.30	25	8	B
	With cumulative impacts (HTP)	0.53	48	14	D

### 3.12 Mitigation and management measures

Overall, the project's construction is expected to have a manageable impact on the surrounding road network. As such, no specific physical mitigation measures are required to facilitate the Project's construction.

A construction traffic management plan (CTMP) and associated traffic guidance schemes will be prepared for the Project as part of the construction environmental management plan. The CTMP will be prepared in consultation with the Muswellbrook Shire Council and emergency services.

In addition, the following management measures are recommended to minimise the Project's traffic impacts during construction:

- **Minimise construction vehicle movements during the weekday PM peak hour:** The intersection of the New England Highway and Hebden Road currently experiences some delay for right-turning vehicles from Hebden Road onto the New England Highway during the PM peak hour; therefore, it is recommended that construction vehicle movements be minimised as much as possible during this period
- **Reduce the speed limit on Hebden Road between the New England Highway and the site access:** Hebden Road is narrow in sections, and an increase in construction vehicle volumes raises the likelihood of two-way heavy vehicle movements needing to pass each other. Therefore, it is recommended that the speed limit be reduced during peak construction activities to minimise road safety risks associated with heavy vehicles passing at high speeds during the construction period.

## 4.0 Operational impact assessment

Once operational, it is anticipated that two staff members would visit the Antienne STSS site on a monthly basis. Therefore, the site would generate up to four vehicle movements per day (two-way), which would have a negligible impact on the surrounding road network.

The proposed Antienne STSS site includes parking provision for two cars and one heavy rigid truck. This parking provision would meet the needs of the Project, particularly considering the site is only expected to generate two workers on-site at one time.



## 5.0 Summary and conclusion

Key outcomes of the operational and construction impact assessment are as follows:

- The peak construction works associated with the Project are expected to generate up to 55 vehicle trips per hour (two-way) during the peak construction activities, which would take place on up to five days across the construction period
- SIDRA INTERSECTION modelling demonstrates that the additional construction traffic associated with the Project would have minor impacts on the surrounding road network during the AM peak hour, with a minor increase in queuing and delay. In the PM peak hour, the New England Highway and Hebden Road intersection would experience increased vehicle delays for the right turn from Hebden Road
- It is recommended that construction activities avoid the PM peak hour to minimise impacts on the New England Highway and Hebden Road intersection
- An Austroads warrant assessment of the new proposed construction site access indicates that a basic right turn treatment is appropriate, and therefore, no auxiliary lanes are required
- During operation, the Project would generate up to two vehicle trips per day, occurring infrequently and having negligible impacts on the surrounding roads, including Hebden Road and the New England Highway.

# Appendix A

## SIDRA INTERSECTION outputs

## Intersection Performance (Existing)

# MOVEMENT SUMMARY

▼ Site: 101v [New England Highway/Hebden Road - AM  
(6:15-7:15am) (Site Folder: Existing AM Peak - 2025)]

Output produced by SIDRA INTERSECTION Version: 9.1.6.228

New Site  
Site Category: (None)  
Give-Way (Two-Way)

Vehicle Movement Performance															
Mov ID	Turn	Mov Class	Demand Flows [ Total HV ] veh/h %		Arrival Flows [ Total HV ] veh/h %		Deg. Satn  v/c	Aver. Delay  sec	Level of Service	95% Back Of Queue [ Veh. Dist ] veh m		Prop. Que	Eff. Stop Rate	Aver. No. of Cycles	Aver. Speed  km/h
South: New England Highway															
2	T1	All MCs	542	14.0	542	14.0	0.152	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	99.9
3	R2	All MCs	19	16.7	19	16.7	0.028	11.6	LOS A	0.1	0.8	0.52	0.73	0.52	59.8
Approach			561	14.1	561	14.1	0.152	0.4	NA	0.1	0.8	0.02	0.02	0.02	97.7
East: Hebden Road															
4	L2	All MCs	9	22.2	9	22.2	0.008	7.4	LOS A	0.0	0.0	0.00	0.63	0.00	62.0
6	R2	All MCs	9	0.0	9	0.0	0.058	27.1	LOS B	0.2	1.2	0.84	0.94	0.84	50.0
Approach			19	11.1	19	11.1	0.058	17.2	LOS B	0.2	1.2	0.42	0.78	0.42	55.4
North: New England Highway															
7	L2	All MCs	52	10.2	52	10.2	0.030	8.1	LOS A	0.0	0.0	0.00	0.66	0.00	70.1
8	T1	All MCs	462	6.6	462	6.6	0.247	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	99.9
Approach			514	7.0	514	7.0	0.247	0.8	NA	0.0	0.0	0.00	0.07	0.00	95.8
All Vehicles			1094	10.7	1094	10.7	0.247	0.9	NA	0.2	1.2	0.02	0.06	0.02	95.5

Site Level of Service (LOS) Method: Delay (RTA NSW). Site LOS Method is specified in the Parameter Settings dialog (Options tab).

Vehicle movement LOS values are based on average delay per movement.

Minor Road Approach LOS values are based on average delay for all vehicle movements.

NA (TWSC): Level of Service is not defined for major road approaches or the intersection as a whole for Two-Way Sign Control (HCM LOS rule).

Two-Way Sign Control Capacity Model: SIDRA Standard.

Delay Model: SIDRA Standard (Control Delay: Geometric Delay is included).

Queue Model: SIDRA queue estimation methods are used for Back of Queue and Queue at Start of Gap.

Gap-Acceptance Capacity Formula: SIDRA Standard (Akçelik M3D).

HV (%) values are calculated for All Movement Classes of All Heavy Vehicle Model Designation.

Arrival Flows used in performance calculations are adjusted to include any Initial Queued Demand and Upstream Capacity Constraint effects.

SIDRA INTERSECTION 9.1 | Copyright © 2000-2024 Akcelik and Associates Pty Ltd | [sidrasolutions.com](http://sidrasolutions.com)

Organisation: AECOM AUSTRALIA PTY LTD | Licence: NETWORK / Enterprise Level 1 | Processed: Wednesday, 16 April 2025 2:18:49 PM  
Project: C:\Users\Jordan.Shiu\OneDrive - AECOM\60751984 HCC REZ\400\_Technical\433\_TechnicalArea\_SIDRA modelling\20250325 - Base Case - var.sip9



# MOVEMENT SUMMARY

▼ Site: 101v [New England Highway/Hebden Road - PM  
(4:30-5:30pm) (Site Folder: Existing PM Peak 2025)]

Output produced by SIDRA INTERSECTION Version: 9.1.6.228

New Site  
Site Category: (None)  
Give-Way (Two-Way)

Vehicle Movement Performance															
Mov ID	Turn	Mov Class	Demand Flows		Arrival Flows		Deg. Satn	Aver. Delay	Level of Service	95% Back Of Queue		Prop. Que	Eff. Stop Rate	Aver. No. of Cycles	Aver. Speed
			[ Total HV ]	%	[ Total HV ]	%	v/c	sec		[ Veh. veh	Dist ] m				km/h
South: New England Highway															
2	T1	All MCs	525	7.0	525	7.0	0.141	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	99.9
3	R2	All MCs	15	7.1	15	7.1	0.026	12.6	LOS A	0.1	0.7	0.58	0.78	0.58	61.4
Approach			540	7.0	540	7.0	0.141	0.4	NA	0.1	0.7	0.02	0.02	0.02	98.2
East: Hebden Road															
4	L2	All MCs	23	9.1	23	9.1	0.018	7.1	LOS A	0.0	0.0	0.00	0.63	0.00	65.7
6	R2	All MCs	28	3.7	28	3.7	0.284	46.4	LOS D	0.8	6.0	0.91	0.99	1.03	39.0
Approach			52	6.1	52	6.1	0.284	28.7	LOS C	0.8	6.0	0.50	0.83	0.57	47.7
North: New England Highway															
7	L2	All MCs	27	3.8	27	3.8	0.015	7.9	LOS A	0.0	0.0	0.00	0.66	0.00	72.8
8	T1	All MCs	638	8.9	638	8.9	0.346	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	99.8
Approach			665	8.7	665	8.7	0.346	0.4	NA	0.0	0.0	0.00	0.03	0.00	98.3
All Vehicles			1257	7.9	1257	7.9	0.346	1.5	NA	0.8	6.0	0.03	0.06	0.03	94.2

Site Level of Service (LOS) Method: Delay (RTA NSW). Site LOS Method is specified in the Parameter Settings dialog (Options tab).

Vehicle movement LOS values are based on average delay per movement.

Minor Road Approach LOS values are based on average delay for all vehicle movements.

NA (TWSC): Level of Service is not defined for major road approaches or the intersection as a whole for Two-Way Sign Control (HCM LOS rule).

Two-Way Sign Control Capacity Model: SIDRA Standard.

Delay Model: SIDRA Standard (Control Delay: Geometric Delay is included).

Queue Model: SIDRA queue estimation methods are used for Back of Queue and Queue at Start of Gap.

Gap-Acceptance Capacity Formula: SIDRA Standard (Akçelik M3D).

HV (%) values are calculated for All Movement Classes of All Heavy Vehicle Model Designation.

Arrival Flows used in performance calculations are adjusted to include any Initial Queued Demand and Upstream Capacity Constraint effects.

SIDRA INTERSECTION 9.1 | Copyright © 2000-2024 Akcelik and Associates Pty Ltd | sidrasolutions.com

Organisation: AECOM AUSTRALIA PTY LTD | Licence: NETWORK / Enterprise Level 1 | Processed: Wednesday, 16 April 2025 3:14:06 PM  
Project: C:\Users\Jordan.Shiu\OneDrive - AECOM\60751984 HCC REZ\400\_Technical\433\_TechnicalArea\_SIDRA modelling\20250325 - Base Case - var.sip9

## Intersection performance (with the Project construction traffic)

# MOVEMENT SUMMARY

Site: 101v [New England Highway/Hebden Road - AM  
(6:15-7:15am) (Site Folder: Construction AM Peak - 2026 )]

Output produced by SIDRA INTERSECTION Version: 9.1.6.228

New Site  
Site Category: (None)  
Give-Way (Two-Way)

Vehicle Movement Performance															
Mov ID	Turn	Mov Class	Demand Flows [ Total HV ] veh/h %		Arrival Flows [ Total HV ] veh/h %		Deg. Satn  v/c	Aver. Delay  sec	Level of Service	95% Back Of Queue [ Veh. Dist ] veh m		Prop. Que	Eff. Stop Rate	Aver. No. of Cycles	Aver. Speed  km/h
South: New England Highway															
2	T1	All MCs	542	14.0	542	14.0	0.152	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	99.9
3	R2	All MCs	34	12.5	34	12.5	0.050	11.7	LOS A	0.2	1.4	0.54	0.76	0.54	60.8
Approach			576	13.9	576	13.9	0.152	0.7	NA	0.2	1.4	0.03	0.04	0.03	96.3
East: Hebden Road															
4	L2	All MCs	11	30.0	11	30.0	0.009	7.5	LOS A	0.0	0.0	0.00	0.63	0.00	60.0
6	R2	All MCs	14	30.8	14	30.8	0.176	53.2	LOS D	0.4	3.8	0.90	0.97	0.94	34.1
Approach			24	30.4	24	30.4	0.176	33.3	LOS C	0.4	3.8	0.51	0.82	0.53	42.0
North: New England Highway															
7	L2	All MCs	89	10.6	89	10.6	0.052	8.1	LOS A	0.0	0.0	0.00	0.66	0.00	69.9
8	T1	All MCs	462	6.6	462	6.6	0.247	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	99.9
Approach			552	7.3	552	7.3	0.247	1.3	NA	0.0	0.0	0.00	0.11	0.00	93.4
All Vehicles			1152	11.1	1152	11.1	0.247	1.7	NA	0.4	3.8	0.03	0.09	0.03	92.4

Site Level of Service (LOS) Method: Delay (RTA NSW). Site LOS Method is specified in the Parameter Settings dialog (Options tab).

Vehicle movement LOS values are based on average delay per movement.

Minor Road Approach LOS values are based on average delay for all vehicle movements.

NA (TWSC): Level of Service is not defined for major road approaches or the intersection as a whole for Two-Way Sign Control (HCM LOS rule).

Two-Way Sign Control Capacity Model: SIDRA Standard.

Delay Model: SIDRA Standard (Control Delay: Geometric Delay is included).

Queue Model: SIDRA queue estimation methods are used for Back of Queue and Queue at Start of Gap.

Gap-Acceptance Capacity Formula: SIDRA Standard (Akçelik M3D).

HV (%) values are calculated for All Movement Classes of All Heavy Vehicle Model Designation.

Arrival Flows used in performance calculations are adjusted to include any Initial Queued Demand and Upstream Capacity Constraint effects.

SIDRA INTERSECTION 9.1 | Copyright © 2000-2024 Akcelik and Associates Pty Ltd | sidrasolutions.com

Organisation: AECOM AUSTRALIA PTY LTD | Licence: NETWORK / Enterprise Level 1 | Processed: Wednesday, 16 April 2025 2:18:51 PM  
Project: C:\Users\Jordan.Shiu\OneDrive - AECOM\60751984 HCC REZ\400\_Technical\433\_TechnicalArea\_SIDRA modelling\20250325 - Base Case - var.sip9

# MOVEMENT SUMMARY

Site: 101 [Hebden Road/Access Road - AM (6:15-7:15am)  
(Site Folder: Construction AM Peak - 2026 )]

Output produced by SIDRA INTERSECTION Version: 9.1.6.228

New Site  
Site Category: (None)  
Give-Way (Two-Way)

Vehicle Movement Performance															
Mov ID	Turn	Mov Class	Demand Flows [ Total HV ] veh/h %		Arrival Flows [ Total HV ] veh/h %		Deg. Satn  v/c	Aver. Delay  sec	Level of Service	95% Back Of Queue [ Veh. Dist ] veh m		Prop. Que	Eff. Stop Rate	Aver. No. of Cycles	Aver. Speed  km/h
South: Access Road															
1	L2	All MCs	5	100.0	5	100.0	0.006	3.9	LOS A	0.0	0.3	0.10	0.47	0.10	31.5
3	R2	All MCs	1	0.0	1	0.0	0.006	4.3	LOS A	0.0	0.3	0.10	0.47	0.10	57.2
Approach			6	83.3	6	83.3	0.006	4.0	LOS A	0.0	0.3	0.10	0.47	0.10	34.0
East: Hebden Road															
4	L2	All MCs	1	0.0	1	0.0	0.011	6.9	LOS A	0.0	0.0	0.00	0.03	0.00	70.4
5	T1	All MCs	19	11.1	19	11.1	0.011	0.0	LOS A	0.0	0.0	0.00	0.03	0.00	79.3
Approach			20	10.5	20	10.5	0.011	0.4	NA	0.0	0.0	0.00	0.03	0.00	79.0
West: Hebden Road															
11	T1	All MCs	71	11.9	71	11.9	0.071	0.0	LOS A	0.3	2.1	0.07	0.27	0.07	74.8
12	R2	All MCs	53	10.0	53	10.0	0.071	6.9	LOS A	0.3	2.1	0.07	0.27	0.07	63.0
Approach			123	11.1	123	11.1	0.071	2.9	NA	0.3	2.1	0.07	0.27	0.07	70.9
All Vehicles			149	14.1	149	14.1	0.071	2.6	NA	0.3	2.1	0.06	0.25	0.06	69.9

Site Level of Service (LOS) Method: Delay (RTA NSW). Site LOS Method is specified in the Parameter Settings dialog (Options tab).

Vehicle movement LOS values are based on average delay per movement.

Minor Road Approach LOS values are based on average delay for all vehicle movements.

NA (TWSC): Level of Service is not defined for major road approaches or the intersection as a whole for Two-Way Sign Control (HCM LOS rule).

Two-Way Sign Control Capacity Model: SIDRA Standard.

Delay Model: SIDRA Standard (Control Delay: Geometric Delay is included).

Queue Model: SIDRA queue estimation methods are used for Back of Queue and Queue at Start of Gap.

Gap-Acceptance Capacity Formula: SIDRA Standard (Akçelik M3D).

HV (%) values are calculated for All Movement Classes of All Heavy Vehicle Model Designation.

Arrival Flows used in performance calculations are adjusted to include any Initial Queued Demand and Upstream Capacity Constraint effects.



# MOVEMENT SUMMARY

▼ Site: 101v [New England Highway/Hebden Road - PM (4:30-5:30pm) (Site Folder: Construction PM Peak - 2026)]

Output produced by SIDRA INTERSECTION Version: 9.1.6.228

New Site  
Site Category: (None)  
Give-Way (Two-Way)

Vehicle Movement Performance															
Mov ID	Turn	Mov Class	Demand Flows [ Total HV ] veh/h %		Arrival Flows [ Total HV ] veh/h %		Deg. Satn  v/c	Aver. Delay  sec	Level of Service	95% Back Of Queue [ Veh. Dist ] veh m		Prop. Que	Eff. Stop Rate	Aver. No. of Cycles	Aver. Speed  km/h
South: New England Highway															
2	T1	All MCs	525	7.0	525	7.0	0.141	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	99.9
3	R2	All MCs	16	13.3	16	13.3	0.030	13.4	LOS A	0.1	0.8	0.60	0.79	0.60	59.0
Approach			541	7.2	541	7.2	0.141	0.4	NA	0.1	0.8	0.02	0.02	0.02	97.9
East: Hebden Road															
4	L2	All MCs	24	13.0	24	13.0	0.019	7.2	LOS A	0.0	0.0	0.00	0.63	0.00	64.5
6	R2	All MCs	33	16.1	33	16.1	0.468	70.8	LOS F	1.2	9.9	0.94	1.03	1.20	30.1
Approach			57	14.8	57	14.8	0.468	43.7	LOS D	1.2	9.9	0.54	0.86	0.69	39.0
North: New England Highway															
7	L2	All MCs	32	16.7	32	16.7	0.019	8.3	LOS A	0.0	0.0	0.00	0.66	0.00	68.1
8	T1	All MCs	638	8.9	638	8.9	0.346	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	99.8
Approach			669	9.3	669	9.3	0.346	0.4	NA	0.0	0.0	0.00	0.03	0.00	97.6
All Vehicles			1267	8.6	1267	8.6	0.468	2.4	NA	1.2	9.9	0.03	0.06	0.04	91.6

Site Level of Service (LOS) Method: Delay (RTA NSW). Site LOS Method is specified in the Parameter Settings dialog (Options tab).

Vehicle movement LOS values are based on average delay per movement.

Minor Road Approach LOS values are based on average delay for all vehicle movements.

NA (TWSC): Level of Service is not defined for major road approaches or the intersection as a whole for Two-Way Sign Control (HCM LOS rule).

Two-Way Sign Control Capacity Model: SIDRA Standard.

Delay Model: SIDRA Standard (Control Delay: Geometric Delay is included).

Queue Model: SIDRA queue estimation methods are used for Back of Queue and Queue at Start of Gap.

Gap-Acceptance Capacity Formula: SIDRA Standard (Akçelik M3D).

HV (%) values are calculated for All Movement Classes of All Heavy Vehicle Model Designation.

Arrival Flows used in performance calculations are adjusted to include any Initial Queued Demand and Upstream Capacity Constraint effects.

SIDRA INTERSECTION 9.1 | Copyright © 2000-2024 Akcelik and Associates Pty Ltd | [sidrasolutions.com](https://www.sidrasolutions.com)

Organisation: AECOM AUSTRALIA PTY LTD | Licence: NETWORK / Enterprise Level 1 | Processed: Wednesday, 16 April 2025 3:14:46 PM  
Project: C:\Users\Jordan.Shiu\OneDrive - AECOM\60751984 HCC REZ\400\_Technical\433\_TechnicalArea\_SIDRA modelling\20250325 - Base Case - var.sip9

# MOVEMENT SUMMARY

▼ Site: 101 [Hebden Road/Access Road - PM (4:30-5:30pm)]  
(Site Folder: Construction PM Peak - 2026)]

Output produced by SIDRA INTERSECTION Version: 9.1.6.228

New Site  
Site Category: (None)  
Give-Way (Two-Way)

Vehicle Movement Performance															
Mov ID	Turn	Mov Class	Demand Flows [ Total HV ] veh/h %		Arrival Flows [ Total HV ] veh/h %		Deg. Satn  v/c	Aver. Delay  sec	Level of Service	95% Back Of Queue [ Veh. Dist ] veh m		Prop. Que	Eff. Stop Rate	Aver. No. of Cycles	Aver. Speed  km/h
South: Access Road															
1	L2	All MCs	5	100.0	5	100.0	0.006	4.1	LOS A	0.0	0.3	0.16	0.46	0.16	31.3
3	R2	All MCs	1	0.0	1	0.0	0.006	4.2	LOS A	0.0	0.3	0.16	0.46	0.16	56.8
Approach			6	83.3	6	83.3	0.006	4.1	LOS A	0.0	0.3	0.16	0.46	0.16	33.9
East: Hebden Road															
4	L2	All MCs	1	0.0	1	0.0	0.028	6.9	LOS A	0.0	0.0	0.00	0.01	0.00	71.1
5	T1	All MCs	52	6.1	52	6.1	0.028	0.0	LOS A	0.0	0.0	0.00	0.01	0.00	79.7
Approach			53	6.0	53	6.0	0.028	0.1	NA	0.0	0.0	0.00	0.01	0.00	79.6
West: Hebden Road															
11	T1	All MCs	42	5.0	42	5.0	0.029	0.1	LOS A	0.1	0.4	0.06	0.09	0.06	77.8
12	R2	All MCs	5	100.0	5	100.0	0.029	8.9	LOS A	0.1	0.4	0.06	0.09	0.06	64.4
Approach			47	15.6	47	15.6	0.029	1.0	NA	0.1	0.4	0.06	0.09	0.06	76.8
All Vehicles			106	14.9	106	14.9	0.029	0.8	NA	0.1	0.4	0.04	0.07	0.04	74.8

Site Level of Service (LOS) Method: Delay (RTA NSW). Site LOS Method is specified in the Parameter Settings dialog (Options tab).

Vehicle movement LOS values are based on average delay per movement.

Minor Road Approach LOS values are based on average delay for all vehicle movements.

NA (TWSC): Level of Service is not defined for major road approaches or the intersection as a whole for Two-Way Sign Control (HCM LOS rule).

Two-Way Sign Control Capacity Model: SIDRA Standard.

Delay Model: SIDRA Standard (Control Delay: Geometric Delay is included).

Queue Model: SIDRA queue estimation methods are used for Back of Queue and Queue at Start of Gap.

Gap-Acceptance Capacity Formula: SIDRA Standard (Akçelik M3D).

HV (%) values are calculated for All Movement Classes of All Heavy Vehicle Model Designation.

Arrival Flows used in performance calculations are adjusted to include any Initial Queued Demand and Upstream Capacity Constraint effects.

# MOVEMENT SUMMARY

Site: 101v [New England Highway/Hebden Road - PM  
(6:00-7:00pm) (Site Folder: Without construction 6 PM - 2026)]

Output produced by SIDRA INTERSECTION Version: 9.1.6.228

New Site  
Site Category: (None)  
Give-Way (Two-Way)

Vehicle Movement Performance															
Mov ID	Turn	Mov Class	Demand Flows		Arrival Flows		Deg. Satn	Aver. Delay	Level of Service	95% Back Of Queue		Prop. Que	Eff. Stop Rate	Aver. No. of Cycles	Aver. Speed
			[ Total HV ]	%	[ Total HV ]	%	v/c	sec		[ Veh. veh	Dist ] m				km/h
South: New England Highway															
2	T1	All MCs	366	8.3	366	8.3	0.099	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	100.0
3	R2	All MCs	6	0.0	6	0.0	0.007	10.1	LOS A	0.0	0.2	0.48	0.66	0.48	66.3
Approach			373	8.2	373	8.2	0.099	0.2	NA	0.0	0.2	0.01	0.01	0.01	99.1
East: Hebden Road															
4	L2	All MCs	17	12.5	17	12.5	0.013	7.2	LOS A	0.0	0.0	0.00	0.63	0.00	64.7
6	R2	All MCs	26	0.0	26	0.0	0.107	19.8	LOS B	0.3	2.4	0.76	0.91	0.76	55.5
Approach			43	4.9	43	4.9	0.107	14.9	LOS B	0.3	2.4	0.46	0.80	0.46	58.8
North: New England Highway															
7	L2	All MCs	13	16.7	13	16.7	0.008	8.3	LOS A	0.0	0.0	0.00	0.66	0.00	67.9
8	T1	All MCs	461	6.4	461	6.4	0.246	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	99.9
Approach			474	6.7	474	6.7	0.246	0.2	NA	0.0	0.0	0.00	0.02	0.00	98.6
All Vehicles			889	7.2	889	7.2	0.246	0.9	NA	0.3	2.4	0.03	0.05	0.03	95.7

Site Level of Service (LOS) Method: Delay (RTA NSW). Site LOS Method is specified in the Parameter Settings dialog (Options tab).

Vehicle movement LOS values are based on average delay per movement.

Minor Road Approach LOS values are based on average delay for all vehicle movements.

NA (TWSC): Level of Service is not defined for major road approaches or the intersection as a whole for Two-Way Sign Control (HCM LOS rule).

Two-Way Sign Control Capacity Model: SIDRA Standard.

Delay Model: SIDRA Standard (Control Delay: Geometric Delay is included).

Queue Model: SIDRA queue estimation methods are used for Back of Queue and Queue at Start of Gap.

Gap-Acceptance Capacity Formula: SIDRA Standard (Akçelik M3D).

HV (%) values are calculated for All Movement Classes of All Heavy Vehicle Model Designation.

Arrival Flows used in performance calculations are adjusted to include any Initial Queued Demand and Upstream Capacity Constraint effects.

# MOVEMENT SUMMARY

▼ Site: 101v [New England Highway/Hebden Road - PM  
(6:00-7:00pm) (Site Folder: With Construction 6 PM - 2026)]

Output produced by SIDRA INTERSECTION Version: 9.1.6.228

New Site  
Site Category: (None)  
Give-Way (Two-Way)

Vehicle Movement Performance															
Mov ID	Turn	Mov Class	Demand Flows		Arrival Flows		Deg. Satn	Aver. Delay	Level of Service	95% Back Of Queue		Prop. Que	Eff. Stop Rate	Aver. No. of Cycles	Aver. Speed
			[ Total HV ]	%	[ Total HV ]	%	v/c	sec		[ Veh. veh	Dist ] m				km/h
South: New England Highway															
2	T1	All MCs	366	8.3	366	8.3	0.099	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	100.0
3	R2	All MCs	7	14.3	7	14.3	0.010	11.0	LOS A	0.0	0.3	0.50	0.68	0.50	61.0
Approach			374	8.5	374	8.5	0.099	0.2	NA	0.0	0.3	0.01	0.01	0.01	98.7
East: Hebden Road															
4	L2	All MCs	32	10.0	32	10.0	0.025	7.1	LOS A	0.0	0.0	0.00	0.63	0.00	65.4
6	R2	All MCs	64	6.6	64	6.6	0.299	25.1	LOS B	1.1	7.8	0.81	0.97	0.97	49.9
Approach			96	7.7	96	7.7	0.299	19.2	LOS B	1.1	7.8	0.55	0.85	0.65	54.2
North: New England Highway															
7	L2	All MCs	17	37.5	17	37.5	0.011	8.8	LOS A	0.0	0.0	0.00	0.66	0.00	61.9
8	T1	All MCs	461	6.4	461	6.4	0.246	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	99.9
Approach			478	7.5	478	7.5	0.246	0.3	NA	0.0	0.0	0.00	0.02	0.00	97.8
All Vehicles			947	7.9	947	7.9	0.299	2.2	NA	1.1	7.8	0.06	0.10	0.07	90.7

Site Level of Service (LOS) Method: Delay (RTA NSW). Site LOS Method is specified in the Parameter Settings dialog (Options tab).

Vehicle movement LOS values are based on average delay per movement.

Minor Road Approach LOS values are based on average delay for all vehicle movements.

NA (TWSC): Level of Service is not defined for major road approaches or the intersection as a whole for Two-Way Sign Control (HCM LOS rule).

Two-Way Sign Control Capacity Model: SIDRA Standard.

Delay Model: SIDRA Standard (Control Delay: Geometric Delay is included).

Queue Model: SIDRA queue estimation methods are used for Back of Queue and Queue at Start of Gap.

Gap-Acceptance Capacity Formula: SIDRA Standard (Akçelik M3D).

HV (%) values are calculated for All Movement Classes of All Heavy Vehicle Model Designation.

Arrival Flows used in performance calculations are adjusted to include any Initial Queued Demand and Upstream Capacity Constraint effects.

SIDRA INTERSECTION 9.1 | Copyright © 2000-2024 Akcelik and Associates Pty Ltd | [sidrasolutions.com](http://sidrasolutions.com)

Organisation: AECOM AUSTRALIA PTY LTD | Licence: NETWORK / Enterprise Level 1 | Processed: Wednesday, 16 April 2025 2:37:00 PM  
Project: C:\Users\Jordan.Shiu\OneDrive - AECOM\60751984 HCC REZ\400\_Technical\433\_TechnicalArea\_SIDRA modelling\20250325 - Base Case - var.sip9

# MOVEMENT SUMMARY

Site: 101 [Hebden Road/Access Road - PM (6:00-7:00pm)  
(Site Folder: With Construction 6 PM - 2026)]

Output produced by SIDRA INTERSECTION Version: 9.1.6.228

New Site  
Site Category: (None)  
Give-Way (Two-Way)

Vehicle Movement Performance															
Mov ID	Turn	Mov Class	Demand Flows [ Total HV ] veh/h %		Arrival Flows [ Total HV ] veh/h %		Deg. Satn  v/c	Aver. Delay  sec	Level of Service	95% Back Of Queue [ Veh. Dist ] veh m		Prop. Que	Eff. Stop Rate	Aver. No. of Cycles	Aver. Speed  km/h
South: Access Road															
1	L2	All MCs	53	10.0	53	10.0	0.036	4.0	LOS A	0.1	1.1	0.12	0.49	0.12	53.0
3	R2	All MCs	1	0.0	1	0.0	0.036	4.1	LOS A	0.1	1.1	0.12	0.49	0.12	57.1
Approach			54	9.8	54	9.8	0.036	4.0	LOS A	0.1	1.1	0.12	0.49	0.12	53.1
East: Hebden Road															
4	L2	All MCs	1	0.0	1	0.0	0.023	6.9	LOS A	0.0	0.0	0.00	0.02	0.00	71.0
5	T1	All MCs	43	4.9	43	4.9	0.023	0.0	LOS A	0.0	0.0	0.00	0.02	0.00	79.7
Approach			44	4.8	44	4.8	0.023	0.2	NA	0.0	0.0	0.00	0.02	0.00	79.6
West: Hebden Road															
11	T1	All MCs	19	11.1	19	11.1	0.017	0.1	LOS A	0.0	0.4	0.09	0.16	0.09	75.9
12	R2	All MCs	5	100.0	5	100.0	0.017	8.9	LOS A	0.0	0.4	0.09	0.16	0.09	61.8
Approach			24	30.4	24	30.4	0.017	2.0	NA	0.0	0.4	0.09	0.16	0.09	73.6
All Vehicles			122	12.1	122	12.1	0.036	2.2	NA	0.1	1.1	0.07	0.25	0.07	67.7

Site Level of Service (LOS) Method: Delay (RTA NSW). Site LOS Method is specified in the Parameter Settings dialog (Options tab).

Vehicle movement LOS values are based on average delay per movement.

Minor Road Approach LOS values are based on average delay for all vehicle movements.

NA (TWSC): Level of Service is not defined for major road approaches or the intersection as a whole for Two-Way Sign Control (HCM LOS rule).

Two-Way Sign Control Capacity Model: SIDRA Standard.

Delay Model: SIDRA Standard (Control Delay: Geometric Delay is included).

Queue Model: SIDRA queue estimation methods are used for Back of Queue and Queue at Start of Gap.

Gap-Acceptance Capacity Formula: SIDRA Standard (Akçelik M3D).

HV (%) values are calculated for All Movement Classes of All Heavy Vehicle Model Designation.

Arrival Flows used in performance calculations are adjusted to include any Initial Queued Demand and Upstream Capacity Constraint effects.



## Intersection performance (with HTP cumulative impact)

# MOVEMENT SUMMARY

▼ Site: 101v [New England Highway/Hebden Road - AM (6:15-7:15am) (Site Folder: Construction AM Peak - 2027 - HTP)]

Output produced by SIDRA INTERSECTION Version: 9.1.6.228

New Site  
Site Category: (None)  
Give-Way (Two-Way)

Vehicle Movement Performance															
Mov ID	Turn	Mov Class	Demand Flows		Arrival Flows		Deg. Satn	Aver. Delay	Level of Service	95% Back Of Queue		Prop. Que	Eff. Stop Rate	Aver. No. of Cycles	Aver. Speed
			[ Total HV ]	%	[ Total HV ]	%	v/c	sec		[ Veh. veh	Dist ] m				km/h
South: New England Highway															
2	T1	All MCs	542	14.0	542	14.0	0.152	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	99.9
3	R2	All MCs	54	45.1	54	45.1	0.105	14.4	LOS A	0.4	3.6	0.58	0.84	0.58	51.1
Approach			596	16.8	596	16.8	0.152	1.3	NA	0.4	3.6	0.05	0.08	0.05	92.0
East: Hebden Road															
4	L2	All MCs	259	8.9	259	8.9	0.203	7.1	LOS A	0.0	0.0	0.00	0.63	0.00	65.7
6	R2	All MCs	14	30.8	14	30.8	0.191	57.7	LOS E	0.5	4.0	0.91	0.98	0.96	32.7
Approach			273	10.0	273	10.0	0.203	9.6	LOS A	0.5	4.0	0.05	0.65	0.05	62.6
North: New England Highway															
7	L2	All MCs	89	10.6	89	10.6	0.052	8.1	LOS A	0.0	0.0	0.00	0.66	0.00	69.9
8	T1	All MCs	462	6.6	462	6.6	0.247	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	99.9
Approach			552	7.3	552	7.3	0.247	1.3	NA	0.0	0.0	0.00	0.11	0.00	93.4
All Vehicles			1420	11.8	1420	11.8	0.247	2.9	NA	0.5	4.0	0.03	0.20	0.03	84.8

Site Level of Service (LOS) Method: Delay (RTA NSW). Site LOS Method is specified in the Parameter Settings dialog (Options tab).

Vehicle movement LOS values are based on average delay per movement.

Minor Road Approach LOS values are based on average delay for all vehicle movements.

NA (TWSC): Level of Service is not defined for major road approaches or the intersection as a whole for Two-Way Sign Control (HCM LOS rule).

Two-Way Sign Control Capacity Model: SIDRA Standard.

Delay Model: SIDRA Standard (Control Delay: Geometric Delay is included).

Queue Model: SIDRA queue estimation methods are used for Back of Queue and Queue at Start of Gap.

Gap-Acceptance Capacity Formula: SIDRA Standard (Akçelik M3D).

HV (%) values are calculated for All Movement Classes of All Heavy Vehicle Model Designation.

Arrival Flows used in performance calculations are adjusted to include any Initial Queued Demand and Upstream Capacity Constraint effects.

# MOVEMENT SUMMARY

▼ Site: 101v [New England Highway/Hebden Road - PM (4:30-5:30pm) (Site Folder: Construction PM Peak - 2027 - HTP)]

Output produced by SIDRA INTERSECTION Version: 9.1.6.228

New Site  
Site Category: (None)  
Give-Way (Two-Way)

Vehicle Movement Performance															
Mov ID	Turn	Mov Class	Demand Flows		Arrival Flows		Deg. Satn	Aver. Delay	Level of Service	95% Back Of Queue		Prop. Que	Eff. Stop Rate	Aver. No. of Cycles	Aver. Speed
			[ Total HV ]	%	[ Total HV ]	%	v/c	sec		[ Veh. veh	Dist ] m				km/h
South: New England Highway															
2	T1	All MCs	525	7.0	525	7.0	0.141	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	99.9
3	R2	All MCs	36	61.8	36	61.8	0.106	18.9	LOS B	0.3	3.7	0.70	0.90	0.70	45.4
Approach			561	10.5	561	10.5	0.141	1.2	NA	0.3	3.7	0.04	0.06	0.04	92.8
East: Hebden Road															
4	L2	All MCs	44	52.4	44	52.4	0.042	7.9	LOS A	0.0	0.0	0.00	0.63	0.00	55.0
6	R2	All MCs	33	16.1	33	16.1	0.511	78.8	LOS F	1.3	10.7	0.95	1.04	1.24	28.3
Approach			77	37.0	77	37.0	0.511	38.0	LOS C	1.3	10.7	0.40	0.80	0.53	39.3
North: New England Highway															
7	L2	All MCs	32	16.7	32	16.7	0.019	8.3	LOS A	0.0	0.0	0.00	0.66	0.00	68.1
8	T1	All MCs	638	8.9	638	8.9	0.346	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	99.8
Approach			669	9.3	669	9.3	0.346	0.4	NA	0.0	0.0	0.00	0.03	0.00	97.6
All Vehicles			1307	11.4	1307	11.4	0.511	3.0	NA	1.3	10.7	0.04	0.09	0.05	88.0

Site Level of Service (LOS) Method: Delay (RTA NSW). Site LOS Method is specified in the Parameter Settings dialog (Options tab).

Vehicle movement LOS values are based on average delay per movement.

Minor Road Approach LOS values are based on average delay for all vehicle movements.

NA (TWSC): Level of Service is not defined for major road approaches or the intersection as a whole for Two-Way Sign Control (HCM LOS rule).

Two-Way Sign Control Capacity Model: SIDRA Standard.

Delay Model: SIDRA Standard (Control Delay: Geometric Delay is included).

Queue Model: SIDRA queue estimation methods are used for Back of Queue and Queue at Start of Gap.

Gap-Acceptance Capacity Formula: SIDRA Standard (Akçelik M3D).

HV (%) values are calculated for All Movement Classes of All Heavy Vehicle Model Designation.

Arrival Flows used in performance calculations are adjusted to include any Initial Queued Demand and Upstream Capacity Constraint effects.

# MOVEMENT SUMMARY

▼ Site: 101v [New England Highway/Hebden Road - PM (6:00-7:00pm) (Site Folder: With Construction 6 PM - 2027 - HTP)]

Output produced by SIDRA INTERSECTION Version: 9.1.6.228

New Site  
Site Category: (None)  
Give-Way (Two-Way)

Vehicle Movement Performance															
Mov ID	Turn	Mov Class	Demand Flows		Arrival Flows		Deg. Satn	Aver. Delay	Level of Service	95% Back Of Queue		Prop. Que	Eff. Stop Rate	Aver. No. of Cycles	Aver. Speed
			[ Total HV ]	%	[ Total HV ]	%	v/c	sec		[ Veh. veh	Dist ] m				km/h
South: New England Highway															
2	T1	All MCs	366	8.3	366	8.3	0.099	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	100.0
3	R2	All MCs	256	8.2	256	8.2	0.330	12.0	LOS A	1.6	12.1	0.59	0.83	0.69	61.8
Approach			622	8.3	622	8.3	0.330	4.9	NA	1.6	12.1	0.24	0.34	0.28	79.7
East: Hebden Road															
4	L2	All MCs	52	44.9	52	44.9	0.047	7.8	LOS A	0.0	0.0	0.00	0.63	0.00	56.6
6	R2	All MCs	64	6.6	64	6.6	0.527	47.5	LOS D	1.8	13.5	0.93	1.05	1.30	38.2
Approach			116	23.6	116	23.6	0.527	29.8	LOS C	1.8	13.5	0.51	0.86	0.72	44.7
North: New England Highway															
7	L2	All MCs	17	37.5	17	37.5	0.011	8.8	LOS A	0.0	0.0	0.00	0.66	0.00	61.9
8	T1	All MCs	461	6.4	461	6.4	0.246	0.0	LOS A	0.0	0.0	0.00	0.00	0.00	99.9
Approach			478	7.5	478	7.5	0.246	0.3	NA	0.0	0.0	0.00	0.02	0.00	97.8
All Vehicles			1216	9.4	1216	9.4	0.527	5.5	NA	1.8	13.5	0.17	0.27	0.21	79.5

Site Level of Service (LOS) Method: Delay (RTA NSW). Site LOS Method is specified in the Parameter Settings dialog (Options tab).

Vehicle movement LOS values are based on average delay per movement.

Minor Road Approach LOS values are based on average delay for all vehicle movements.

NA (TWSC): Level of Service is not defined for major road approaches or the intersection as a whole for Two-Way Sign Control (HCM LOS rule).

Two-Way Sign Control Capacity Model: SIDRA Standard.

Delay Model: SIDRA Standard (Control Delay: Geometric Delay is included).

Queue Model: SIDRA queue estimation methods are used for Back of Queue and Queue at Start of Gap.

Gap-Acceptance Capacity Formula: SIDRA Standard (Akçelik M3D).

HV (%) values are calculated for All Movement Classes of All Heavy Vehicle Model Designation.

Arrival Flows used in performance calculations are adjusted to include any Initial Queued Demand and Upstream Capacity Constraint effects.
